




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 07/19/2024 - 07/26/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	3	100.0	0.06		95-100
#8 (2.36mm)	3	99.7	0.10		85-100
#16 (1.18mm)	3	96.0	0.80	67-98	65-99
#30 (.6mm)	3	76.1	3.38	27-79	25-80
#50 (.3mm)	3	31.9	4.62	7-38	5-40
#100 (.15mm)	3	2.8	0.90	0-6	0-7
#200 (75µm)	3	0.1	0.00		0-4
Pan	3	0.0	0.00		
FM	3	1.93	0.096	1.87-2.18\2	1.85-2.2
Total Moisture	3	3.8	1.37		
D10 (ES)	3	0.1789	0.00737		
D50	3	0.40	0.025		
D60	3	0.47	0.025		
Cc	3	0.99	0.081		
Cu	3	2.60	0.067		

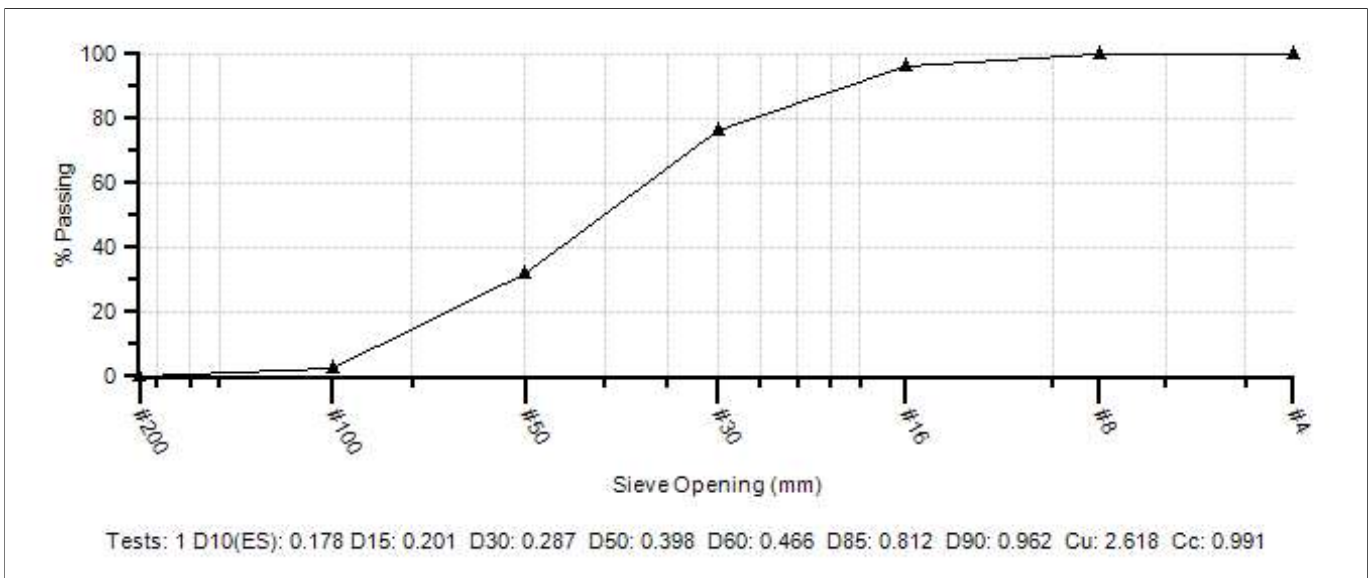

Query

Query Selections
Date Created 07/26/2024
Date Range 07/19/2024 - 07/26/2024
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
