




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 10/11/2024 - 10/18/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	7	100.0	0.04		95-100
#8 (2.36mm)	7	99.7	0.08		85-100
#16 (1.18mm)	7	95.0	0.33	67-98	65-99
#30 (.6mm)	7	71.8	1.42	27-79	25-80
#50 (.3mm)	7	29.8	1.82	7-38	5-40
#100 (.15mm)	7	2.5	0.35	0-6	0-7
#200 (75µm)	7	0.1	0.07		0-4
Pan	7	0.0	0.00		
FM	7	2.01	0.040	1.87-2.18\2	1.85-2.2
Total Moisture	7	3.2	0.30		
D10 (ES)	7	0.1816	0.00329		
D50	7	0.42	0.013		
D60	7	0.49	0.013		
Cc	7	1.00	0.032		
Cu	7	2.72	0.031		

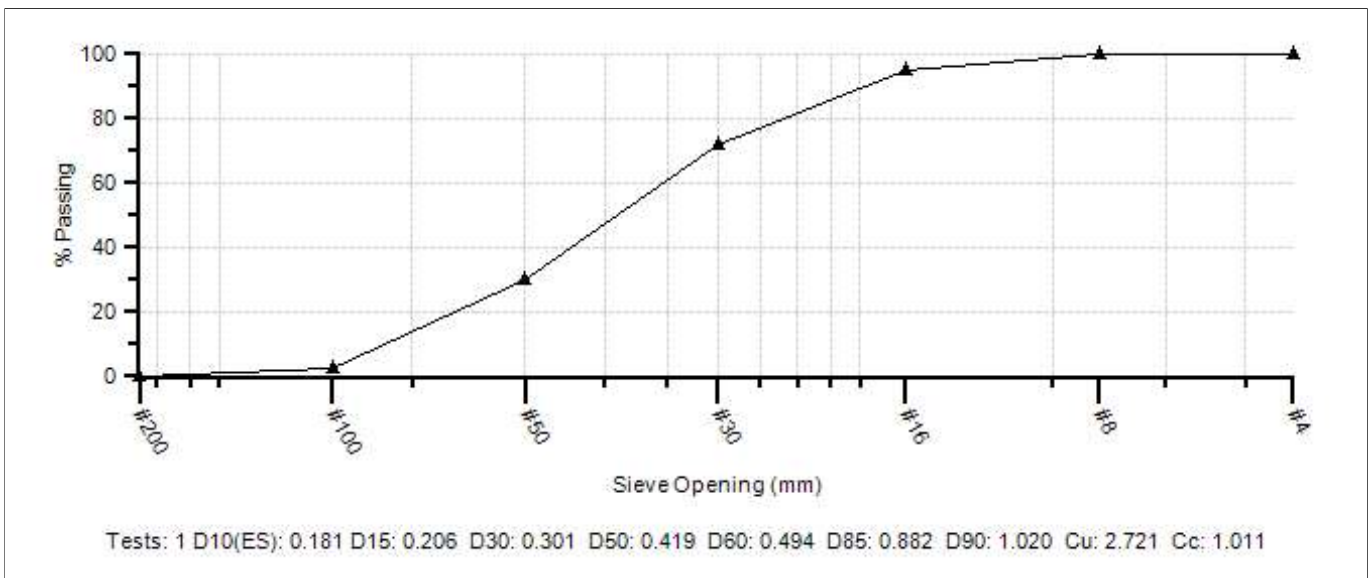

Query

Query Selections
Date Created 10/18/2024
Date Range 10/11/2024 - 10/18/2024
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
